University of Nebraska - Lincoln
DigitalCommons@University of Nebraska - Lincoln

US Army Corps of Engineers, Omaha District | US Department of Defense

1-1-2007

U.S. Army Corps of Engineers Omaha District Monthly Drought Report, November 2007

Follow this and additional works at: http://digitalcommons.unl.edu/usarmyceomaha

Part of the Civil and Environmental Engineering Commons

"U.S. Army Corps of Engineers Omaha District Monthly Drought Report, November 2007" (2007). *US Army Corps of Engineers, Omaha District.* Paper 130.
http://digitalcommons.unl.edu/usarmyceomaha/130

This Article is brought to you for free and open access by the US Department of Defense at DigitalCommons@University of Nebraska - Lincoln. It has been accepted for inclusion in US Army Corps of Engineers, Omaha District by an authorized administrator of DigitalCommons@University of Nebraska - Lincoln.

U.S. Army Corps of Engineers

Omaha District

Monthly Drought Report

November 2007

US Army Corps
of Engineers
Omaha District

Table of Contents

Current Conditions 3

Drought Outlook 10

Ft. Peck, Montana
- Reservoir Elevation Overview 13
- Water Intake Overview 14
- Access Overview 14
- Noxious Weeds Overview 14
- Cultural Resources Overview 14

Garrison, North Dakota
- Reservoir Elevation Overview 15
- Water Intake Overview 16
- Access Overview 18
- Boat Ramp Information 19
- Noxious Weeds Overview 21
- Cultural Resources Overview 21
- Other Areas of Interest/Concern 21

Oahe, South Dakota
- Reservoir Elevation Overview 22
- Water Intake Overview 23
- Access Overview 24
- Noxious Weeds Overview 24
- Cultural Resources Overview 24

Mainstem Reservoir Information, Weekly Elevation Comparison
- 3 SEPT 2007 through 24 SEPT 2007 25

Mainstem Reservoir Storage Comparison Water Years 2004, 2005, 2006, 2007
- Ft. Peck, MT 27
- Garrison, ND 28
- Oahe, SD 29

Cover Photo: Rock Creek Marina of Ft. Peck Lake

CURRENT CONDITIONS

Similar to the past several months, a review of the drought indicators leads to the conclusion that the drought conditions in the basin continue to improve. Much needed moisture was received throughout the summer and fall and this is reflected in the extent and severity of the drought conditions indicated. Also similar to the past several months, the upper three mainstem reservoirs continue to operate well below their designated conservation pools. Ft. Peck is 33.7 feet below, Garrison is 24.3 feet below, and Oahe is 26.6 feet below the top of conservation pool, respectively. Also, it appears that no municipal intakes on the reservoirs are in jeopardy of running out of water in the foreseeable future.

Precipitation Departures

Precipitation departures from normal during the last 72 months for the United States are shown in Figure 1. The figure indicates that large portions of the basin are moving towards "normal" or even a surplus of moisture.

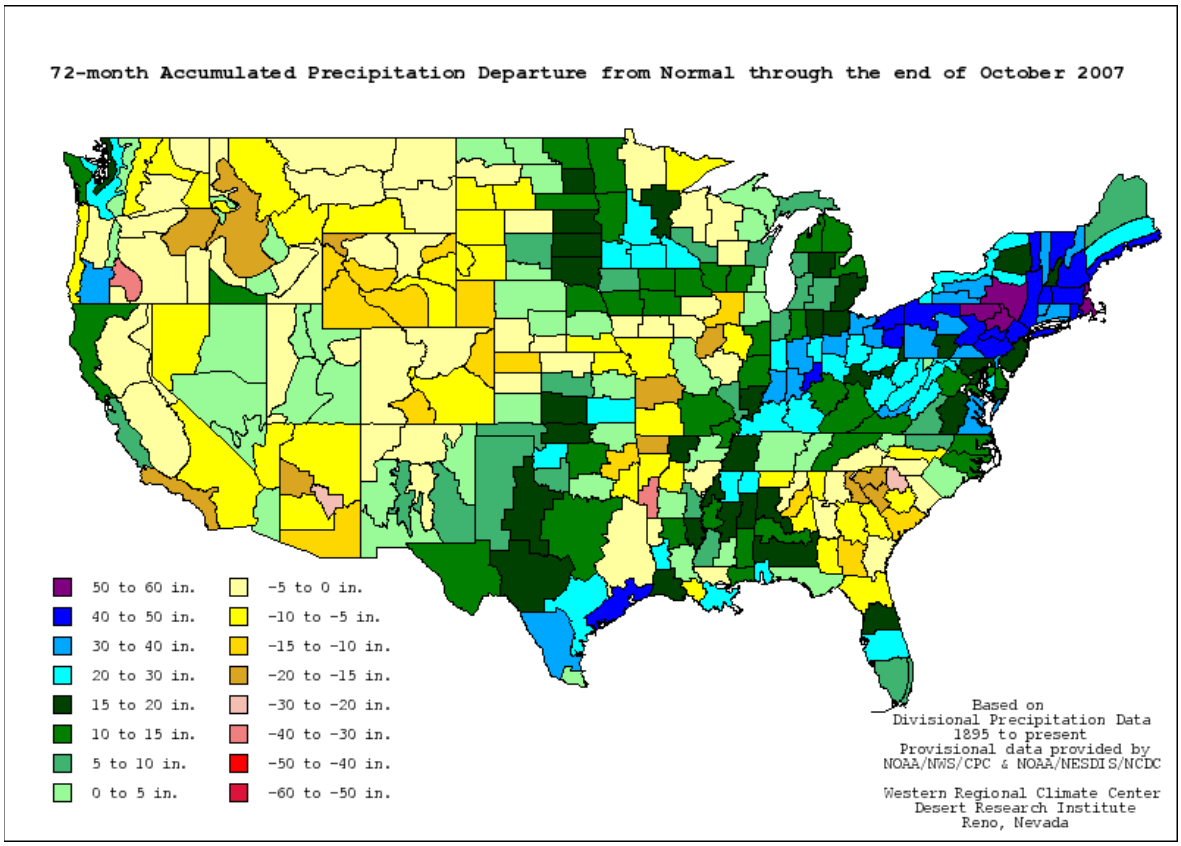

Figure 1 – 72 month Precipitation Departure From Normal
http://www.wrcc.dri.edu/cgi-bin/spiFmap.pl?dep72

Figure 2 indicates that the annual precipitation accumulation in the basin is beginning to trend towards normal to surplus precipitation amounts.

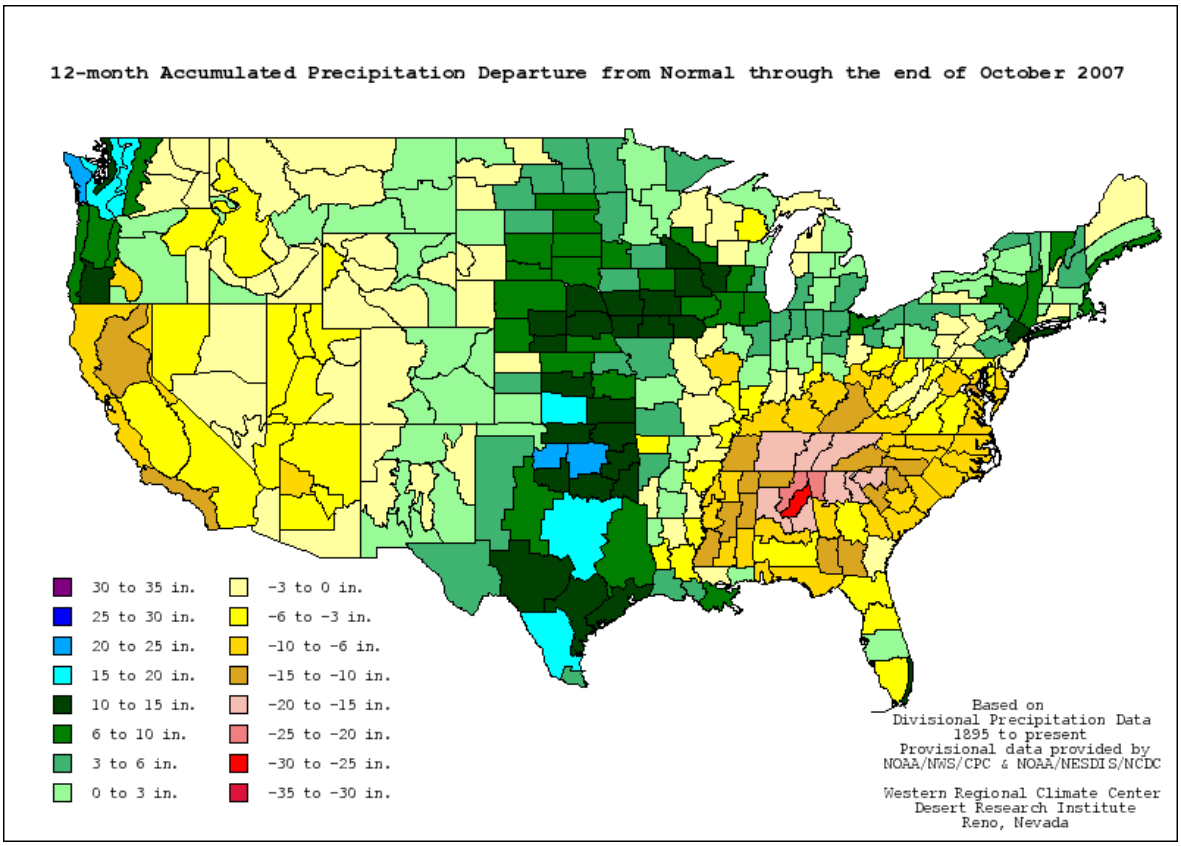

Figure 2 – 12 month Precipitation Departure From Normal
http://www.wrcc.dri.edu/cgi-bin/spiFmap.pl?dep12

The three-month period (Figure 3) shows that much of the basin is trending towards "normalcy" or even a surplus of moisture.

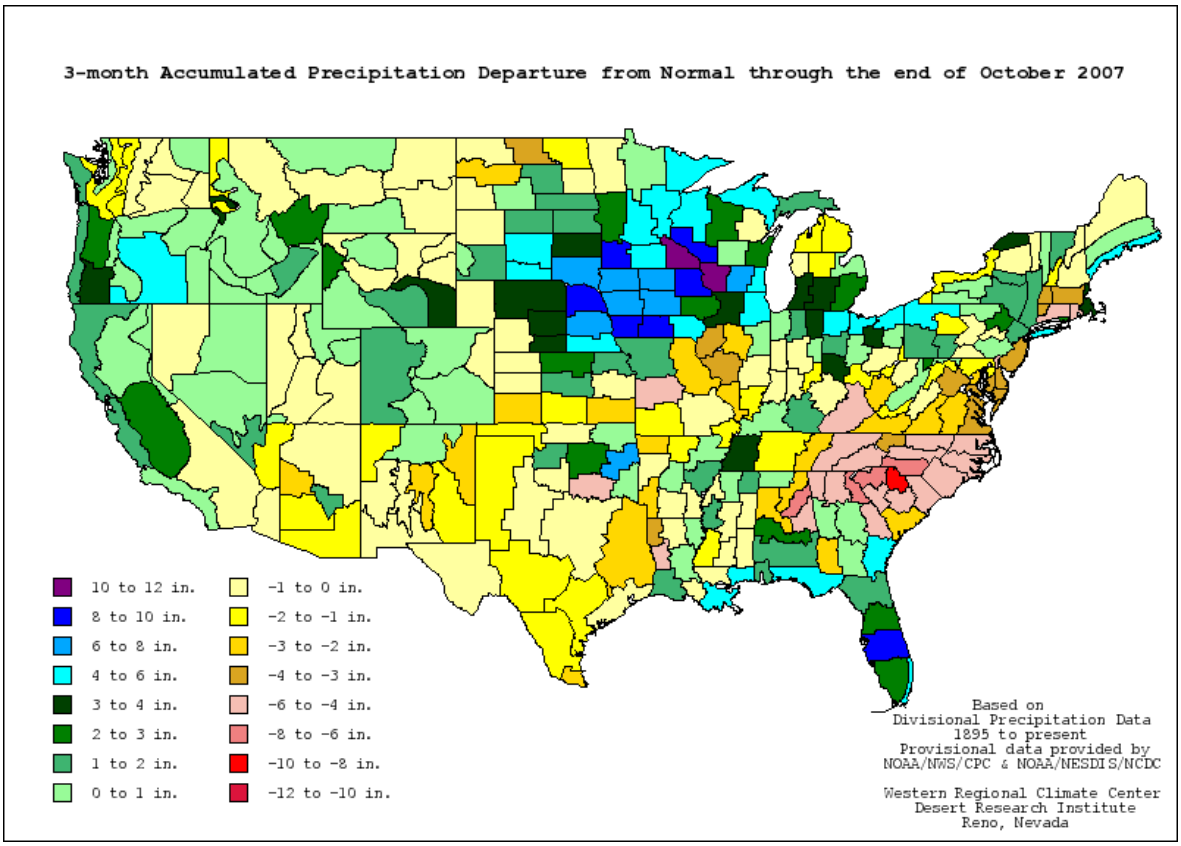

Figure 3 – 3 month Precipitation Departure From Normal
http://www.wrcc.dri.edu/cgi-bin/spiFmap.pl?dep03

For the month of October, generally, the basin received nearly average rainfall, which is indicated in the following figure (Figure 4).

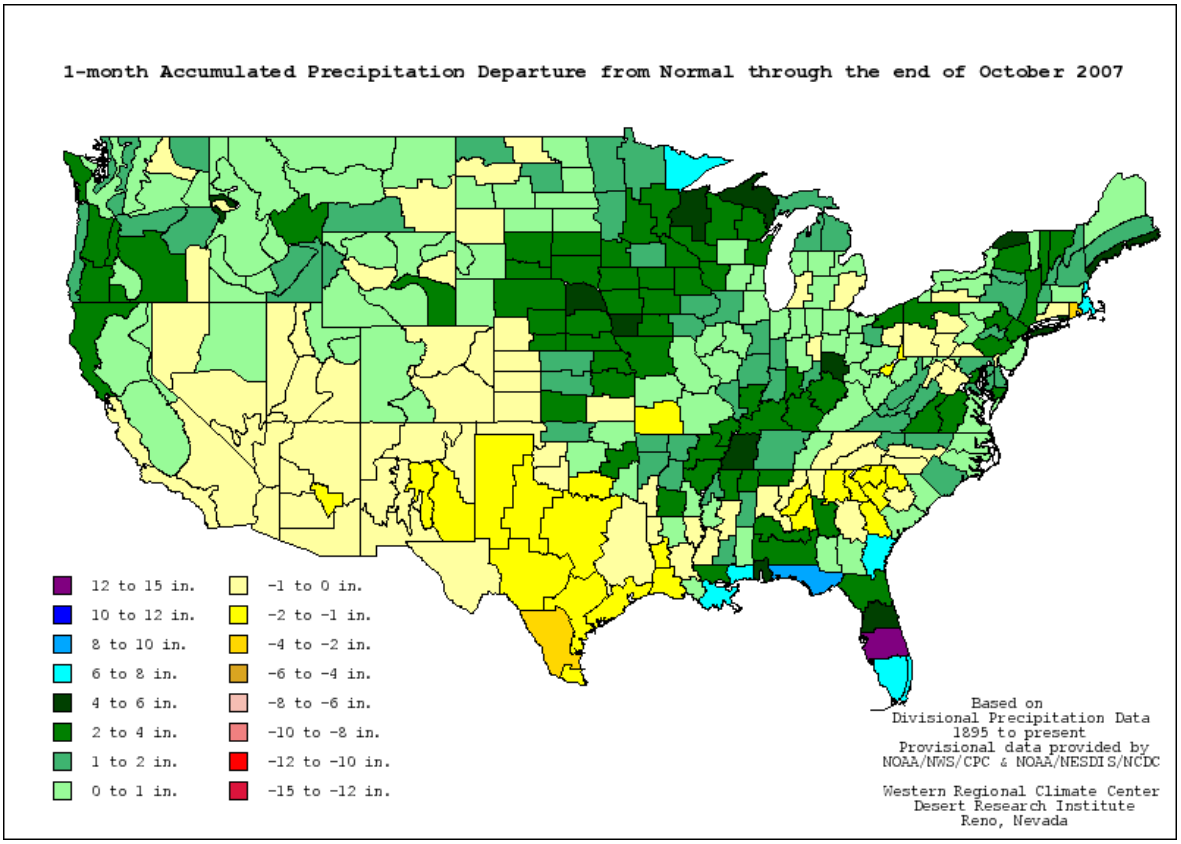

Figure 4 – 1 month Precipitation Departure From Normal
http://www.wrcc.dri.edu/cgi-bin/spiFm8yap.pl?dep01

Drought Indicators

The Palmer Drought Severity Index and the Drought Monitor are two commonly used drought-indicator products that convey both short-term and long-term drought conditions and impacts. Both the Palmer Index and Drought Monitor depict some regions exhibiting varying degrees of drought in Nebraska, South Dakota, Wyoming, and Montana, which have been suffering from drought since 2000.

Palmer Drought Severity Index

The Palmer Drought Severity Index (PDSI) is a meteorological drought index that monitors the hydrologic water balance including the basic terms such as precipitation, evapotranspiration, soil recharge, runoff, and moisture loss. The purpose of this index is to provide standardized measurements of the moisture balance in a region without taking into account streamflow, lake and reservoir levels, and other hydrologic impacts. PDSI is a multi-month drought index; therefore, it responds well and is more suitable for short-term droughts.

Changes to the PDSI are more immediate in response to heavy precipitation over short periods. Figure 5 indicates that large portions of the basin is receiving near normal or even a surplus of short-term moisture.

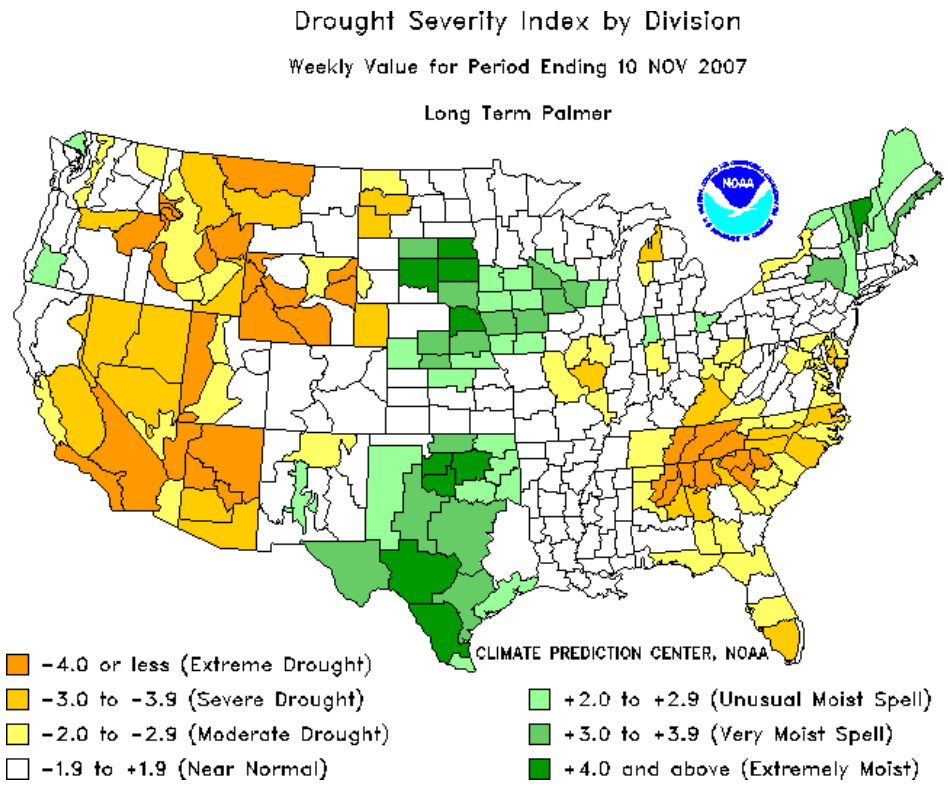

Figure 5 – Long-Term Palmer Drought Indicator Ending 10 November 2007
http://www.cpc.ncep.noaa.gov/products/analysis_monitoring/regional_monitoring/palmer.gif

Drought Monitor

The Drought Monitor is a multi-agency comprehensive drought classification scheme updated weekly by the National Drought Mitigation Center. The Drought Monitor combines information from the Palmer Drought Index, the Climate Prediction Center's soil moisture model, USGS weekly streamflow percentiles, the standard precipitation index, the crop moisture index, and during the snow season basin snow water content, basin average precipitation, and the surface water supply index. Since this product considers streamflow conditions and reservoir water supply, and it allows manual adjustment; it is a good depiction of long-term drought impacts to the affected areas. The Drought Monitor uses four levels of drought classification (moderate, severe, extreme, and exceptional), and it notes the type of impact caused by the drought (agricultural and hydrologic).

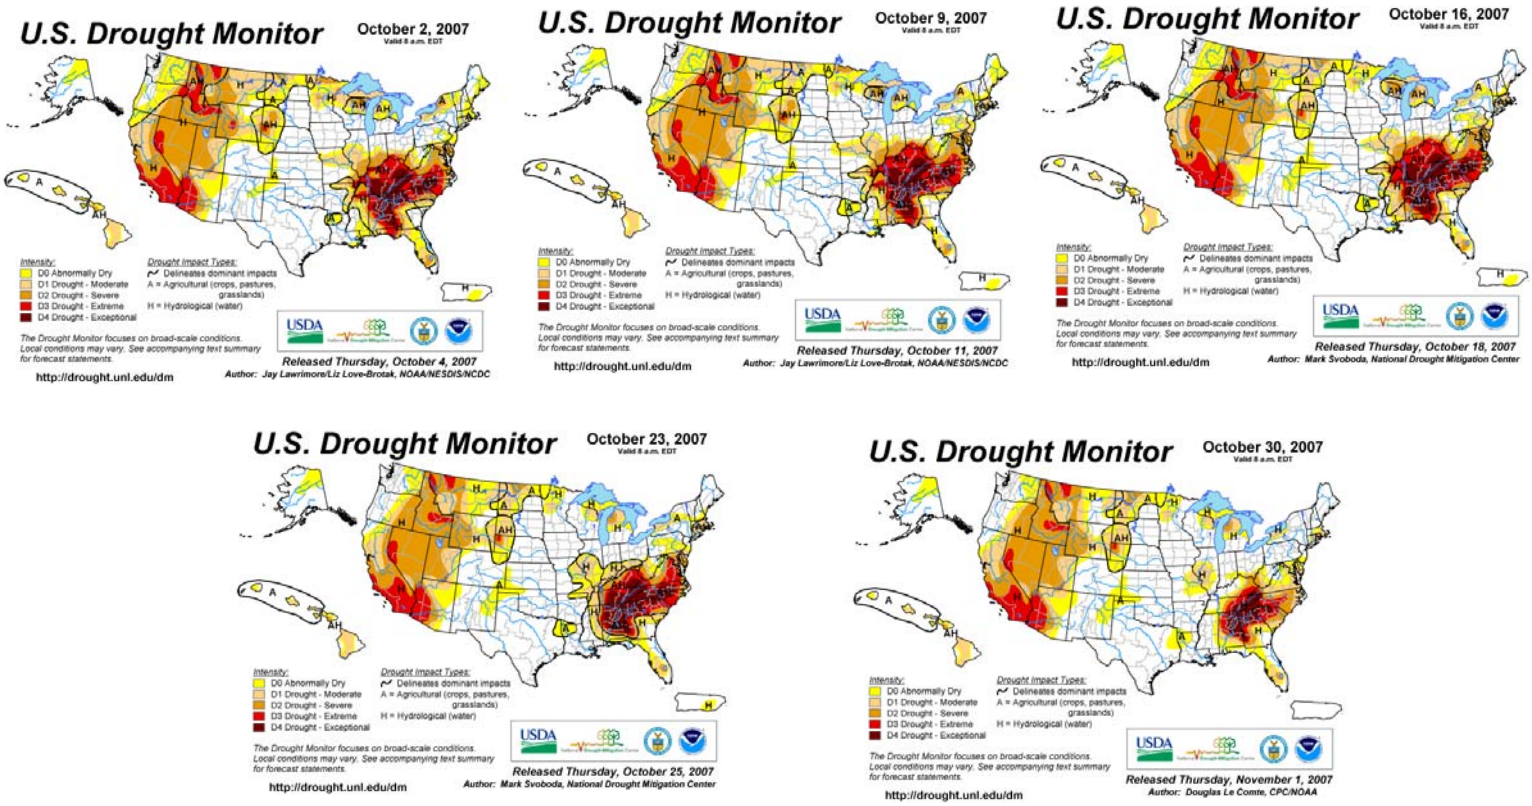

Figure 6 – U.S. Drought Monitor – October 2, 2007 through October 30, 2007
http://www.drought.unl.edu/dm/monitor.html

DROUGHT OUTLOOK

The basin drought outlook uses several expert products that indicate precipitation needs necessary to reduce the Palmer Drought to normal conditions, a one- and three-month climate outlook, and the impacts that future climate predictions could have on the current drought situation.

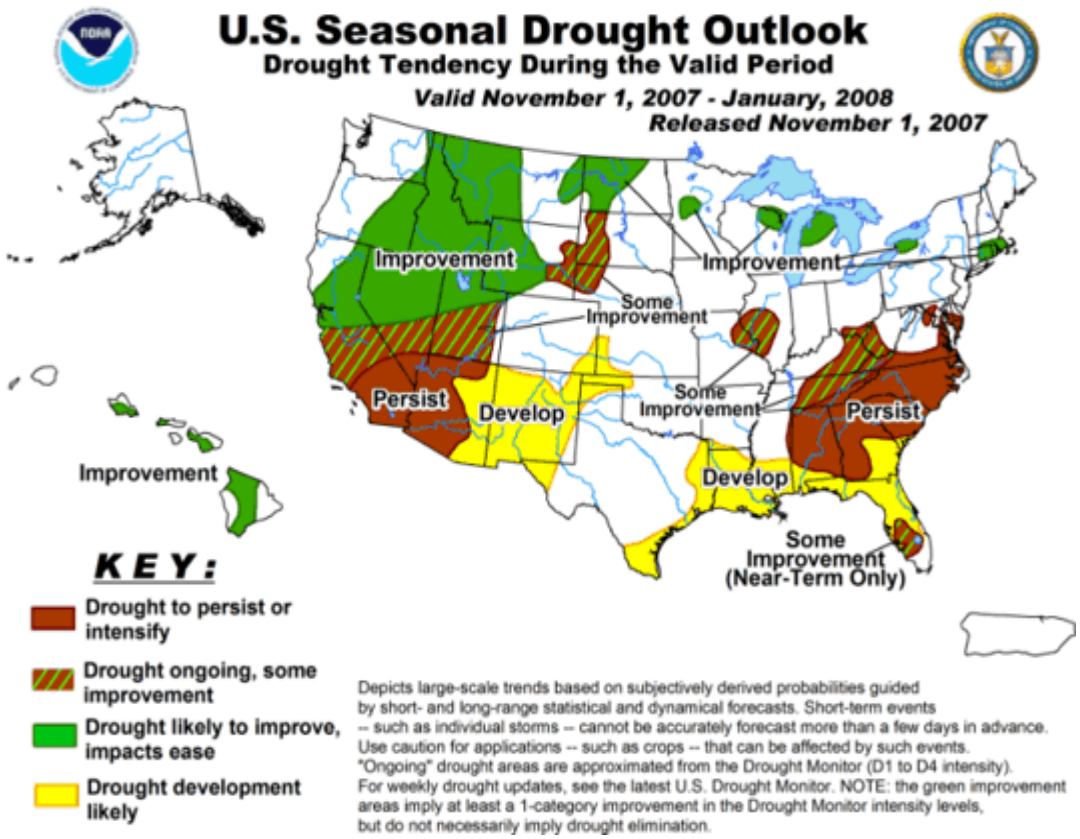

Figure 7 – Three-Month Seasonal Drought Outlook through January 2008
http://www.cpc.ncep.noaa.gov/products/expert_assessment/seasonal_drought.html

Weekly Precipitation Need

Figure 8 is the weekly precipitation needed to reduce the current Palmer Drought Severity Index value to -0.5 or near normal conditions.

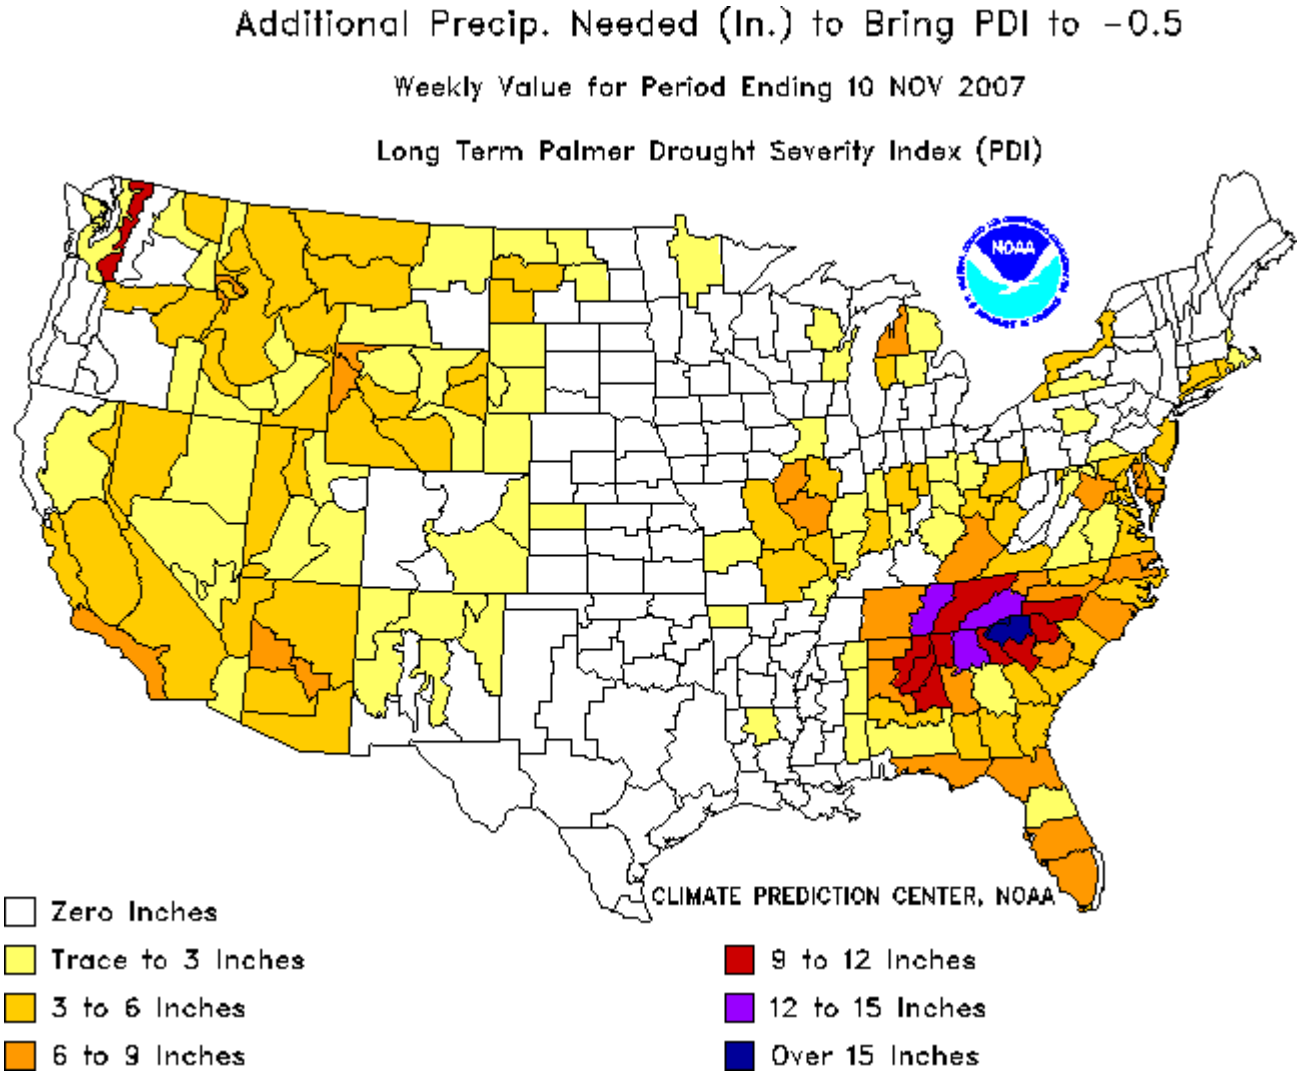

Figure 8 – Weekly Precipitation Need to Bring PDI to -0.5
http://www.cpc.ncep.noaa.gov/products/analysis_monitoring/regional_monitoring/addpcp.gif

Mainstem Reservoir Information

During the month of October the upper three mainstem reservoirs remained at a relatively constant elevation; well above their record lows. Ft. Peck rose 0.2 feet, Garrison fell 0.5 feet and the Oahe reservoir fell 0.1 feet.

Fort Peck, Montana

Reservoir Elevation Overview

Lake Elevation 10/31/2006 (ft. msl)	Current Lake Elevation 10/31/2007 (ft. msl)	30-Day Projected Elevation (11/30/2007) (ft. msl)	120-Day Projected Elevation (02/29/2008) (ft. msl)
2202.4	2200.3	2199.7	2198.4

Comments:

1. Current reservoir elevation is 33.7-feet below the top of conservation pool (elevation 2234.0 ft. msl).
2. Projections provided are based upon the Lower Basic Simulation prepared by the Reservoir Control Center.
3. Current elevation is 2.1-feet lower than 10/31/06 (2202.4).
4. The elevation of 2196.2 is the current record low.

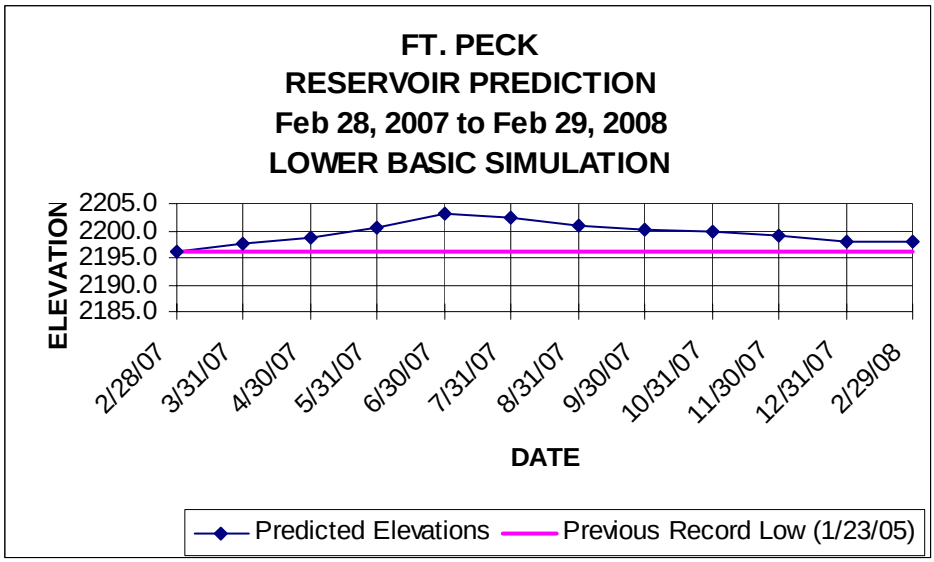

Water Intake Overview

Intake	Comments
Hell Creek State Park	No issues. Well completed 22 NOV 2004

Access Overview

1. 15 ramps usable; 3 ramps unusable. No permanent ramps operational.
2. $250,000 programmed for boat ramp extensions/maintenance in FY 2007.
3. Once the reservoir is free of ice, the boat ramps will be extended to provide the most optimum access possible given the current reservoir conditions.

Boat Ramp	Status	Bottom Elevation	Top Elevation	Managing Agency
Fort Peck Marina	USABLE	2197	2250	COE/Concessionaire
Duck Creek	USABLE	2197	2250	COE/MTFW&P
Flat Lake	USABLE	2197	2250	COE
Rock Creek (North Fork)	USABLE	2197	2250	COE/MTFW&P
Rock Creek Marina	USABLE	2197	2250	Concessionaire
Nelson Creek	UNUSABLE	2220 (Cannot Be Extended)	2250	COE
Hell Creek	USABLE	2197	2250	COE/MTFW&P
Devils Creek	USABLE	2197	2250	COE
Crooked Creek	UNUSABLE	2223 (Cannot Be Extended)	2250	Concessionaire
Fourchette	UNUSABLE	2204 (Cannot Be Extended)	2250	COE
Bone Trail	USABLE	2197	2250	COE
Pines	USABLE	2197	2250	COE
James Kipp	USABLE	Missouri River, Upstream of Dam		BLM
Floodplain	USABLE	Missouri River, Below Dam		COE
Roundhouse Point	USABLE	Missouri River, Below Dam		COE
Nelson Dredge	USABLE	Missouri River, Below Dam		COE
Trout Pond	USABLE	Missouri River, Below Dam		MTFW&P
Rock Creek West	USABLE	Missouri River, Upstream of Dam		USFWS

Noxious Weeds Overview

1. As the reservoir elevation dropped, the noxious weeds spread along the shoreline.
2. Main concern is Saltcedar, which thrives along the shoreline as the reservoir elevation declines.
3. $200,000 programmed for noxious weed control in FY 2008.

Cultural Resources Overview

1. No issues to date.

Garrison, North Dakota

Reservoir Elevation Overview

Lake Elevation 10/31/2006 (ft. msl)	Current Lake Elevation 10/31/2007 (ft. msl)	30-Day Projected Elevation (11/30/2007) (ft. msl)	120-Day Projected Elevation (02/29/2008) (ft. msl)
1809.6	1813.2	1812.8	1808.0

Comments:

1. Current reservoir elevation is 24.3-feet below the top of conservation pool (elevation 1837.5 ft. msl).
2. Projections provided are based upon the Lower Basic Simulation prepared by the Reservoir Control Center.
3. Current reservoir elevation is 3.6-feet higher than elevation on 10/31/06 (1809.6).
4. Record low for the reservoir is 1805.76 on May 12, 2005.

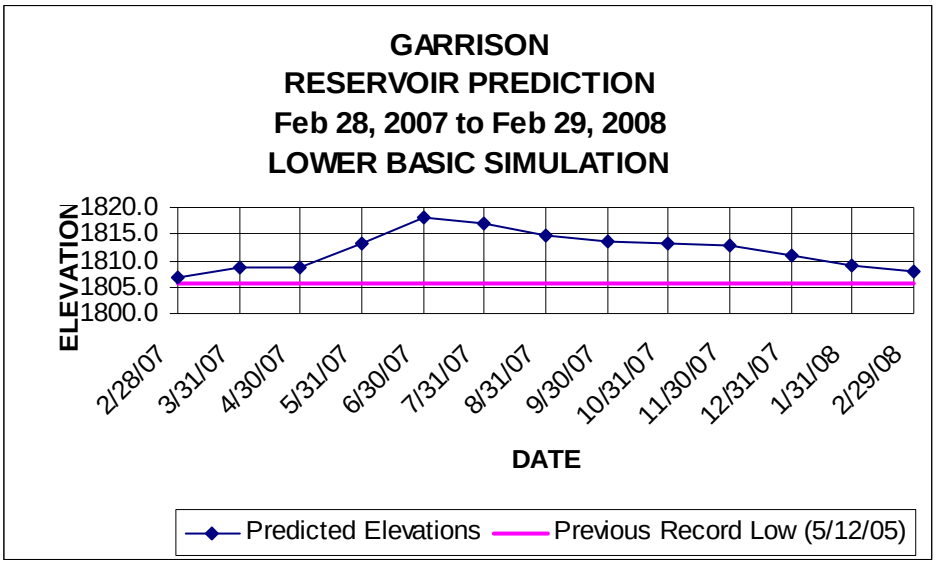

Water Intake Overview

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Whiteshield	Operational	1813.2	1787	1805	1794	1796	720	N	TAT/BOR

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005. The intake was extended and lowered 2-feet since the Corps' survey in 2005.
2. Operation concern level corresponds to previous record lows where erosion of newly exposed shoreline may cause problems with erosion at the intake.
3. A new intake was to be installed in 2007. The new elevation and operational information will be provided when available.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Twin Buttes	Operational	1813.2	1784.4	1805	1788	1790	425	N	TAT/BOR

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. Erosion due to low reservoir levels have caused increased sediment in the intake piping. This has increased maintenance cost to remove the sediment and increased the cost of treating the water.
3. A new intake was to be installed in 2007. The new elevation and operational information will be provided when available.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Mandaree	Operational	1813.2	1786	1789.0	1789	1794	780	N	TAT/BOR

Comments:

1. The new intake screen is at elevation 1786.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Four Bears	Operational	1813.2	1789.9	1800.0	1792	1794	900	N	TAT/BOR

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. Erosion due to low reservoir levels have caused increased sediment in the intake piping. This has increased maintenance cost to remove the sediment and increased the cost of treating the water.
3. A new intake was to be installed in 2007. The new elevation and operational information will be provided when available.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Parshall	Operable	1813.2	1803.6*	1806.6	1797.5	1801.5	1000	N	Parshall

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. The City had a telescoping riser attached to the intake by 30 July 2005. The riser extended the intake to within 3- to 4-feet of the water's surface.
3. Require at least 3 feet of water over the intake for proper operation.
4. Water quality at current level is good following water treatment.
5. Technical Assistance Report was completed by the Corps of Engineers for Parshall in December 2006.
6. A backup well is available for use should the intake fail. The well has been used successfully in the past.

Future Plans:

1. Discussions have been held between Parshall and New Town regarding future water supply. No formal decisions have been reached. Parshall is a proposed supplier for the Rural Water System.

*Screen is raised or lowered according to reservoir elevations.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Pick City	Operational	1813.2	1795	1800	1798	1800	200		Pick City

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. At least 5-feet of water is necessary to operate this intake. If continued usage is planned, the intake will have to be lowered.

Future Plans:

1. Rural water is available to the City, however, they have chosen to continue using their intake until the water no longer meets State Health Standards or work is required on their intake.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Garrison	Operational	1813.2	1787.2	1805	1792	1792	1830	N	Garrison

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. A regulatory permit was currently issued for the reinstallation of existing 950-feet of 8” poly pipe and installation of new 250-feet of 8” poly pipe to extend the intake system.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
SW Pipeline	Operational	1813.2	1779.0	1782	1776		34,000	N	SW Pipeline

Comments:

1. This system provides water for the City of Dickinson, Antelope Valley Power Plant, Coal Gasification Plant, and the Southwest Water Authority.

Access Overview

1. Ft. Stevenson State Park Marina bids were opened and the contract was awarded. Work is to begin during the Fall of 2007 and be completed in FY 2009.

The following table provides the updated boat ramp status on Lake Sakakawea.

Updated 11/5/2007

Reservoir Elevation 10/31/07 – 1813.2

Location	Type	Top Elevation	Bottom Elevation	Comments	Managing Agency	Contact Person	Phone
Beaver Bay (low-water-COE)	poured concrete	1829	1808	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Beulah Bay	poured concrete	1852.4	1799	**Usable**	Beulah Park Board	Bev Sullivan	873-5852
Camp of the Cross	Slide-in metal sections	1819	1806	**Usable**	Lutheran Bible Camp	Larry Crowder	337-2246
Charging Eagle Bay (1st low water)	poured concrete	1829.2	1810.6	**Unusable (Can be extended)**	Three Affiliated Tribes	Jim Mossett	880-1203
Dakota Waters Resort (low-water)	poured concrete, planks	1853.4	1802.6	**Usable**	Beulah Park Board	Kelvin Heinsen	873-5800
Deepwater Creek (2nd low water)	concrete planks & metal	1820	1805.5	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Deepwater Creek (1st low water)	poured concrete	1838.5	1809	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Douglas Creek (low water)	poured concrete, planks	1831	1790	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Fort Stevenson State Park (low water)	poured concrete	1821.8	1790	**Usable**	ND Parks & Rec	Dick Messerly	337-5576
Four Bears Park (south low water)	concrete planks	1820.7	1805.5	**Usable**	Three Affiliated Tribes	Alan Chase	627-4018
Garrison Creek Cabin Site	poured concrete	1857	1802	**Usable**	Garrison Cabin Assc.	Percy Radke	337-2247
Government Bay (low water)	slide-in metal sections	1815	1803	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Government Bay (main ramp)	poured concrete	1857	1810	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Hazen Bay (2nd low water)	poured concrete	1830.6	1808	**Usable**	Hazen Park Board	Mannie Hendrickson	748-5958
Indian Hills (2nd low water)	concrete planks	1817.6	1807	**Usable**	Parks & Rec/Tribes	Kelly Sorge	743-4122
Indian Hills (3rd low water)	Will need to reinstall	1810	1795				
McKenzie Bay (east ramp)	poured concrete	1850.9	1796	**Usable**	McKenzie Marine Club	Rhonda Logan	579-3366

Location	Type	Top Elevation	Bottom Elevation	Comments	Managing Agency	Contact Person	Phone
New Town (proposed ramp)	slide-in metal sections	1819.0	1806.0	**Usable**	New Town Park Board	Dusty Rhodes	627-3900
Parshall Bay (2nd low-water)	slide-in metal sections	1817.8	1808.5	**Usable**	Mountrail County Park Board	Clarence Weltz	627-3377
Pouch Point (3rd low-water)	slide-in metal sections	1819	1807	**Usable**	Three Affiliated Tribes	Paul Danks	627-3627
Pouch Point (2nd low-water)	poured concrete	1834.8	1813	**Unusable**	Three Affiliated Tribes	Paul Danks	627-3627
Reunion Bay (2nd low water)	concrete planks	1826.6	1808	**Usable**	Corps of Engineers	Linda Phelps	654-7411
Sakakawea State Park (main)	poured concrete	1850	1800	**Usable**	ND Parks & Rec	John Tunge	487-3315
Sakakawea State Park (low water)	will need to finish ramp	1807	1790				
Sanish Bay (Aftem) (low water)	poured concrete	1830.8	1807.4	**Usable**	Aftem Lake Development	Gerald Aftem	852-2779
Skunk Creek Recreation Area (main)	poured concrete	1840	1806.5	**Usable**	Three Affiliated Tribes	Ken Danks	290-2841
Sportsmen's Centennial Park	poured concrete	1831.6	1808.5	**Usable**	McLean County	Les Korgel	462-8541
Sportsmen's Centennial Park (2nd low water)	slide-in metal sections	1810	1795	**Usable**			
Steinke Bay	poured concrete	1833.1	1813.4	**Unusable**	North Dakota Game & Fish	Bob Frohlich	328-6346
Van Hook (Gull Island south low-water)	metal bridge deck sections	1817.8	1805	**Usable**	Mountrail County Park Board	Clarence Weltz	627-3377
Van Hook (west low water ramps)	poured concrete	1821.2	1808	**Usable**	Mountrail County Park Board	Clarence Weltz	627-3377
White Earth Bay (main)	poured concrete	1850.9	1801	**Usable**	Mountrail County Park Board	Greg Gunderson	755-3277
Wolf Creek Recreation Area (1st low water)	poured concrete	1833.8	1802.5	**Usable**	Corps of Engineers	Linda Phelps	654-7411

Noxious Weeds Overview

1. Project personnel are continuing efforts to combat noxious weeds.
2. $123,000 programmed for noxious weed control in FY 2008.

Cultural Resources Overview

1. Corps and Tribal personnel continue to monitor the shoreline for exposure of cultural site and opportunities for protection of sites.

Other Areas of Interest/Concern

1. Garrison National Fish Hatchery – Three issues exist and are of concern to the State of North Dakota and the U.S. Fish and Wildlife Service.
    a. Addition of a fifth boiler and necessary power for operation.
    b. Ability to fill 40 rearing ponds.
    c. Adequacy of the existing 20-inch water supply line from the penstocks.
2. Fact sheets for the hatchery issues exist. OP-TM is investigating a design for additional power requirements to the hatchery. An MOU may need to be set up to address future operating needs and requirements.

Oahe, South Dakota

Reservoir Elevation Overview

Lake Elevation 10/31/2006 (ft. msl)	Current Lake Elevation 10/31/2007 (ft. msl)	30-Day Projected Elevation (11/30/2007) (ft. msl)	120-Day Projected Elevation (02/29/2008) (ft. msl)
1572.5	1580.9	1582.1	1581.4

Comments:

1. Current reservoir elevation is 26.6-feet below the top of conservation pool (elevation 1607.5 ft. msl).
2. Projections provided are based upon the Lower Basic Simulation prepared by the Reservoir Control Center.
3. Current reservoir elevation is 8.4-feet higher than 10/31/06 (1572.5).
4. Record low for the reservoir is 1570.17 on August 31, 2006.

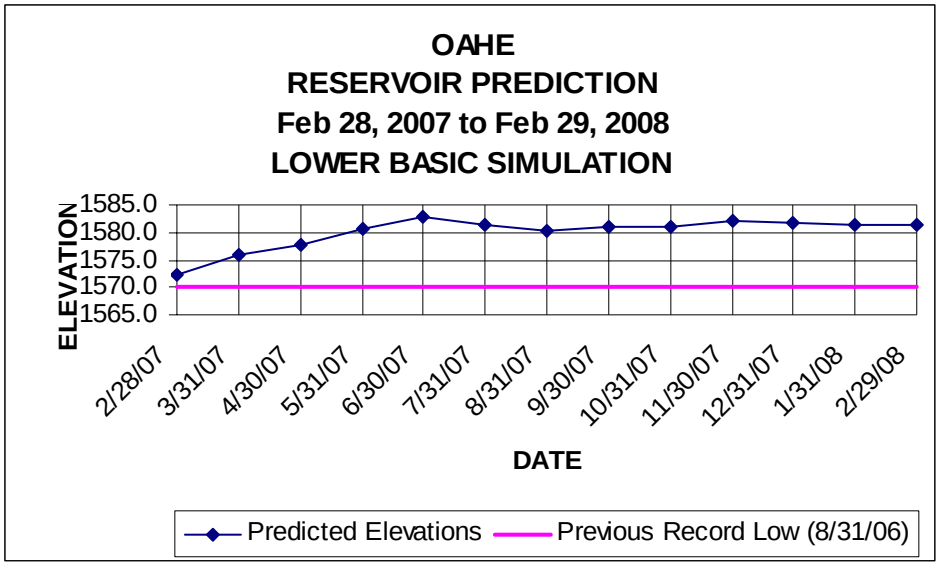

Water Intake Overview

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Ft. Yates	Operational	1580.9	1571.2	1573	1572.2*	1575.2*	3,400	Y	SRST/BOR

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005.
2. A backup well has been drilled and tested.
3. New well and plumbing is installed at Fort Yates and can be used as a backup water source.

*Intake is in riverine conditions and flow to the intake may be influenced by releases from Garrison reservoir.

Future Plans:

1. The intake at Fort Yates remains in a river condition and may continue to have sedimentation problems as long as Oahe remains below elevation 1580. Sediment levels in the sump are measured weekly and the river channel is monitored.
2. Contingency plans are in place and have been exercised.

Intake	Status	Current Reservoir Elev.	Top of Screen Elev.	Operational Concern Elev.	Shutdown Elev.		Population Supported	Contingency Plan? (Y/N)	Resp. Agency
					Summer	Winter			
Wakpala	Operational	1580.9	1563	1563	1566	1569	>500	N	SRST/BOR

Comments:

1. Top of Screen Elevation taken from survey completed by the Corps in 2005, a new low profile screen was installed lowering the top of the screen elevation to 1563, this elevation was confirmed in February 2007.
2. Contingency plans are being drafted to respond to an intake failure. Initial response to an intake failure at Wakpala would be hauling water from the city of Mobridge to the treatment plant to be distributed using the existing transmission lines.

Access Overview

1. The State of South Dakota is responsible for maintaining recreational areas and access to the reservoir in South Dakota. The Oahe Project maintains the access in North Dakota. To view ramp status on Oahe in South Dakota, click on the following link:
   Oahe Boat Ramp Status in South Dakota

2. Ramps on Oahe Project in North Dakota:

AREA	Status
Sibley Park	Unusable
Little Heart Bottoms	Unusable
Kimball (Desert)	Marginal
Graner's Bottoms	Usable
Maclean Bottoms	Usable
Hazelton	Usable
Ft. Rice	Usable
North Beaver Bay	Usable
Walker Bottoms	Usable
Jennerville (Rivery)	Usable
Fort Yates	Unusable
Cattail Bay	Unusable
Langeliers Bay	Unusable
Beaver Creek	Unusable
State Line	Unusable

http://www.gf.nd.gov/boating/mo-riv-system-boatramps-status.html

Noxious Weeds Overview

1. $225,000 programmed for noxious weed control in FY 2008.

Cultural Resources Overview

1. Corps and Tribal personnel continue to monitor the shoreline for exposure of cultural site and opportunities for protection of sites.

Mainstem Reservoir Information, Weekly Elevation Comparison

1 Oct. 2007	Project Information		Reservoir Elevation			Reservoir Storage		
Project	Multi-Purpose Pool Elev.	Flood Control Pool Elev.	Current Elevation (10/1/07)	Previous Elevation (9/24/07)	Change	Current Storage (MAC-FT) (10/1/07)	Previous Storage (MAC-FT) (9/24/07)	Change (MAC-FT)
Ft. Peck, MT	2160 - 2246	2246 – 2250	2200.3	2200.3	0.0	9.040	9.056	-0.016
Garrison, ND	1775 – 1850	1850 – 1854	1813.7	1814.0	-0.3	11.828	11.828	-0.062
Oahe, SD	1540 - 1617	1617 – 1620	1580.9	1580.9	0.0	11.873	11.873	0.054
Big Bend, SD	1415 – 1422	1422 – 1423	1420.8	1420.7	0.1	1.670	1.670	-0.001
Ft. Randall, SD	1320 – 1365	1365 – 1375	1343.6	1346.9	-3.3	2.911	2.911	-0.249
Gavins Point, SD	1204.5 - 1208	1208 - 1210	1207.3	1206.9	0.4	0.382	0.382	0.007

8 Oct. 2007	Project Information		Reservoir Elevation			Reservoir Storage		
Project	Multi-Purpose Pool Elev.	Flood Control Pool Elev.	Current Elevation (10/8/07)	Previous Elevation (10/1/07)	Change	Current Storage (MAC-FT) (10/8/07)	Previous Storage (MAC-FT) (10/1/07)	Change (MAC-FT)
Ft. Peck, MT	2160 - 2246	2246 – 2250	2200.4	2200.3	0.1	9.058	9.040	0.018
Garrison, ND	1775 – 1850	1850 – 1854	1813.6	1813.7	-0.1	11.727	11.828	-0.039
Oahe, SD	1540 - 1617	1617 – 1620	1580.9	1580.9	0.0	11.927	11.873	-0.028
Big Bend, SD	1415 – 1422	1422 – 1423	1420.8	1420.8	0.0	1.669	1.670	0.007
Ft. Randall, SD	1320 – 1365	1365 – 1375	1341.3	1343.6	-2.3	2.662	2.911	-0.136
Gavins Point, SD	1204.5 - 1208	1208 - 1210	1207.7	1207.3	0.4	0.389	0.382	0.013

15 Oct. 2007	Project Information		Reservoir Elevation			Reservoir Storage		
Project	Multi-Purpose Pool Elev.	Flood Control Pool Elev.	Current Elevation (10/15/07)	Previous Elevation (10/8/07)	Change	Current Storage (MAC-FT) (10/15/07)	Previous Storage (MAC-FT) (10/8/07)	Change (MAC-FT)
Ft. Peck, MT	2160 - 2246	2246 – 2250	2200.3	2200.4	-0.1	9.042	9.058	-0.016
Garrison, ND	1775 – 1850	1850 – 1854	1813.5	1813.6	-0.1	11.701	11.727	-0.026
Oahe, SD	1540 - 1617	1617 – 1620	1580.9	1580.9	0.0	11.882	11.927	-0.017
Big Bend, SD	1415 – 1422	1422 – 1423	1420.9	1420.8	0.1	1.676	1.669	0.0
Ft. Randall, SD	1320 – 1365	1365 – 1375	1340.1	1341.3	-1.2	2.449	2.662	-0.077
Gavins Point, SD	1204.5 - 1208	1208 - 1210	1208.0	1207.7	0.3	0.412	0.389	0.010

22 Oct. 2007	Project Information		Reservoir Elevation			Reservoir Storage		
Project	Multi-Purpose Pool Elev.	Flood Control Pool Elev.	Current Elevation (10/22/07)	Previous Elevation (10/15/07)	Change	Current Storage (MAC-FT) (10/22/07)	Previous Storage (MAC-FT) (10/15/07)	Change (MAC-FT)
Ft. Peck, MT	2160 - 2246	2246 – 2250	2200.3	2200.3	0.0	9.042	9.042	0.0
Garrison, ND	1775 – 1850	1850 – 1854	1813.4	1813.5	-0.1	11.701	11.701	-0.007
Oahe, SD	1540 - 1617	1617 – 1620	1580.7	1580.9	-0.2	11.882	11.882	-0.022
Big Bend, SD	1415 – 1422	1422 – 1423	1421.2	1420.9	0.3	1.676	1.676	0.014
Ft. Randall, SD	1320 – 1365	1365 – 1375	1342.8	1340.1	2.7	2.449	2.449	0.167
Gavins Point, SD	1204.5 - 1208	1208 - 1210	1208.3	1208.0	0.3	0.421	0.412	0.009

29 Oct. 2007	Project Information		Reservoir Elevation			Reservoir Storage		
Project	Multi-Purpose Pool Elev.	Flood Control Pool Elev.	Current Elevation (10/29/07)	Previous Elevation (10/22/07)	Change	Current Storage (MAC-FT) (10/29/07)	Previous Storage (MAC-FT) (10/22/07)	Change (MAC-FT)
Ft. Peck, MT	2160 - 2246	2246 – 2250	2200.3	2200.3	0.0	9.040	9.042	-0.002
Garrison, ND	1775 – 1850	1850 – 1854	1813.3	1813.4	-0.1	11.655	11.701	-0.039
Oahe, SD	1540 - 1617	1617 – 1620	1580.8	1580.7	0.1	11.874	11.882	0.014
Big Bend, SD	1415 – 1422	1422 – 1423	1420.9	1421.2	-0.3	1.674	1.676	-0.016
Ft. Randall, SD	1320 – 1365	1365 – 1375	1343.9	1342.8	1.1	2.685	2.449	0.069
Gavins Point, SD	1204.5 - 1208	1208 - 1210	1207.5	1208.3	-0.8	0.396	0.421	-0.025

Mainstem Reservoir Storage Comparison – Water Years 2004, 2005, 2006, 2007

Fort Peck, Montana

Water Year 2004 (FEB 2004 - JAN 2005)		Water Year 2005 (FEB 2005 - JAN 2006)		Water Year 2006 (FEB 2006 - JAN 2007)		Water Year 2007 (FEB 2007 - JAN 2008)	
Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)
2204	9.603	2198.3	8.732	2200.4	9.048	2197.5	8.618
2205.5	9.837	2198.6	8.773	2201.5	9.222	2196.3	8.440
2204.9	9.740	2198.6	8.773	2203.5	9.540	2197.5	8.619
2203.4	9.507	2199.6	8.935	2205.5	9.741	2198.8	8.804
2203.8	9.565	2203.0	9.448	2206.3	9.962	2200.8	9.103
2202.4	9.357	2203.2	9.472	2206.2	9.958	2203.1	9.465
2200.9	9.121	2202.2	9.325	2204.9	9.750	2202.3	9.342
2199.8	8.969	2202.0	9.286	2203.6	9.525	2200.9	9.122
2199.8	8.963	2202.6	9.371	2202.5	9.359	2200.3	9.040
2199.8	8.961	2202.9	9.432	2202.6	9.383	2200.3	9.034
2198.9	8.829	2201.6	9.223	2199.4	8.913		
2198.5	8.749	2201.0	9.134	2199.4	8.907		

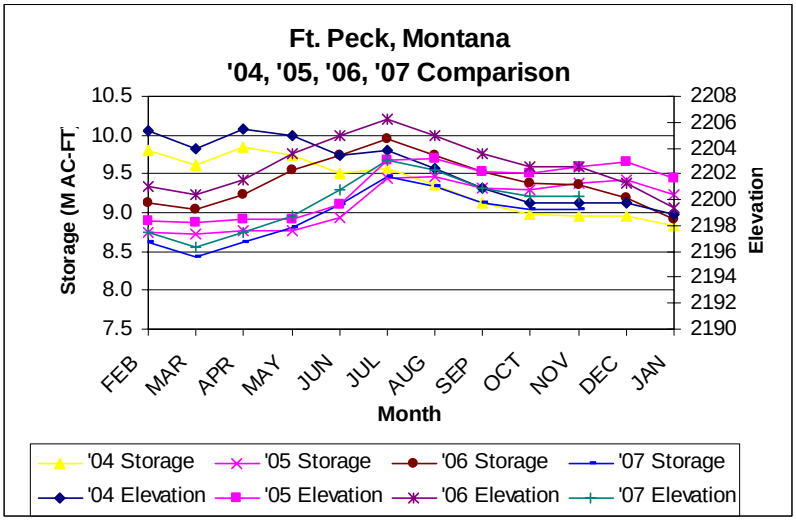

Garrison, ND

Water Year 2004 (FEB 2004 - JAN 2005)		Water Year 2005 (FEB 2005 - JAN 2006)		Water Year 2006 (FEB 2006 - JAN 2007)		Water Year 2007 (FEB 2007 - JAN 2008)	
Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)
1814.3	11.891	1808.2	10.538	1811.4	11.040	1807.0	10.277
1815.6	12.197	1808.7	10.632	1810.6	11.076	1806.9	10.241
1814.7	11.989	1806.6	10.189	1810.7	11.460	1808.7	10.631
1815.3	12.121	1808.8	10.665	1812.5	11.992	1808.6	10.612
1816.5	12.426	1814.9	12.026	1817.3	12.628	1813.1	11.612
1816.5	12.401	1817.2	12.591	1817.4	12.629	1818.1	12.774
1814.3	11.914	1815.8	12.216	1815.5	12.172	1816.9	12.514
1813.3	11.645	1814.1	11.861	1812.1	11.372	1814.6	11.999
1813.1	11.589	1814.0	11.837	1809.5	10.838	1813.7	11.766
1812.3	11.422	1813.5	11.707	1809.6	10.822	1813.2	11.636
1810.0	10.936	1812.0	11.368	1807.8	10.441		
1808.4	10.574	1811.4	11.222	1807.8	10.439		

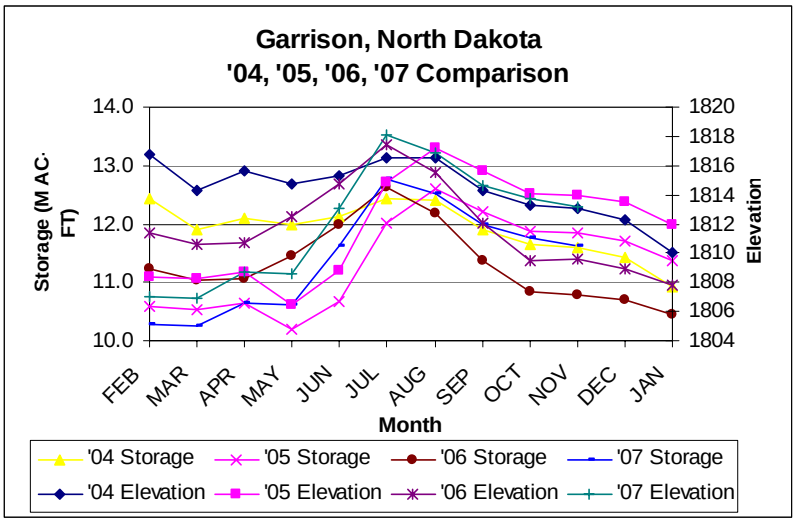

Oahe, SD
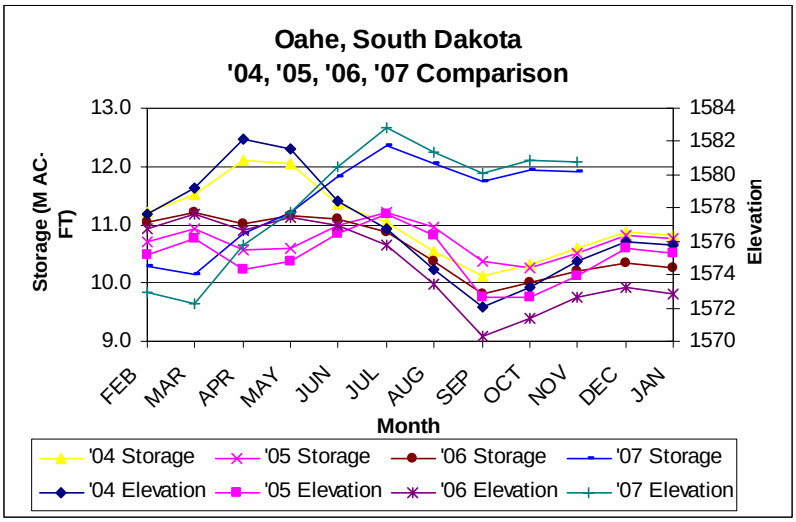
Water Year 2004 (FEB 2004 - JAN 2005)		Water Year 2005 (FEB 2005 - JAN 2006)		Water Year 2006 (FEB 2006 - JAN 2007)		Water Year 2007 (FEB 2007 - JAN 2008)	
Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)	Elevation	Storage (MAC-Ft.)
1577.6	11.204	1575.2	10.715	1576.8	11.037	1572.9	10.287
1579.2	11.504	1576.2	10.924	1577.6	11.209	1572.3	10.151
1582.1	12.110	1574.29	10.568	1576.7	11.024	1575.8	10.839
1581.6	12.056	1574.82	10.608	1577.4	11.150	1577.7	11.221
1578.4	11.338	1576.47	10.980	1577.0	11.088	1580.5	11.826
1576.8	11.045	1577.6	11.214	1575.8	10.881	1582.8	12.346
1574.3	10.540	1576.38	10.958	1573.4	10.378	1581.4	12.045
1572.1	10.112	1572.6	10.363	1570.3	9.807	1580.1	11.752
1573.2	10.316	1572.63	10.267	1571.4	9.998	1580.9	11.927
1574.8	10.608	1573.9	10.501	1572.6	10.214	1580.8	11.898
1576	10.866	1575.6	10.814	1572.9	10.263		
1575.8	10.824	1575.3	10.75	1572.8	10.260
